

Weekly Construction Update

Nov 24 - 28, 2014



Minnesota State Capitol Restoration Project

Architectural Integrity. Building
Functionality. Life Safety.

What's New on Site this Week?

Exterior

- Highly-carved detail pieces are arriving on site this week. They will be installed and blended into existing marble.

Interior

- Structural demolition in shafts and stone walls is ramping up to create vertical and horizontal pathways. This work is loud and involves shoring and supporting the existing structure until new steel is installed.

Continuing Activities

Exterior

- Main roof repair efforts are wrapping up for the season.
- North Wing: Marble repair and restoration continues.
- West Wing: Marble repair and restoration continues.

Interior

- Underground work intensifies through mid-December.
- Demolition activities continue.
- Basement: Concrete slab removal and foundation underpinning continues. Miscellaneous asbestos removal continues. Mechanical, electrical, plumbing installation continues.

Images of the Week Page 2

Getting Around the Capitol Page 3

- What to Expect
- What's Open
- What's Closed

Anticipated Noise and Disturbances

Exterior

- Expect noise, machinery, workers, scaffolding, closed sidewalks.

Interior

- West elevator services Ground through 3rd floors only and the Basement is closed to the public effective August 29 – December.
- Underground noise, vibration and corridor reconfiguration intensifies through mid-November.

Looking Ahead – Three Weeks Out

Exterior

- Installing more directional signage outside of the Capitol to better guide visitors through construction areas.
- Window work for Phase II will be complete.

Interior

- Structural demolition uses large saws. As the work moves through the building there will be some new noises.
- Construction activity accelerates through mid-November.
- Office walls being built on the basement level.

Featured Notice

Did you know that the marble used for the State Capitol weighs
180 pounds per cubic foot?


Images of the Week

Nov 24 - 28, 2014



Minnesota State Capitol Restoration Project

Architectural Integrity. Building
Functionality. Life Safety.

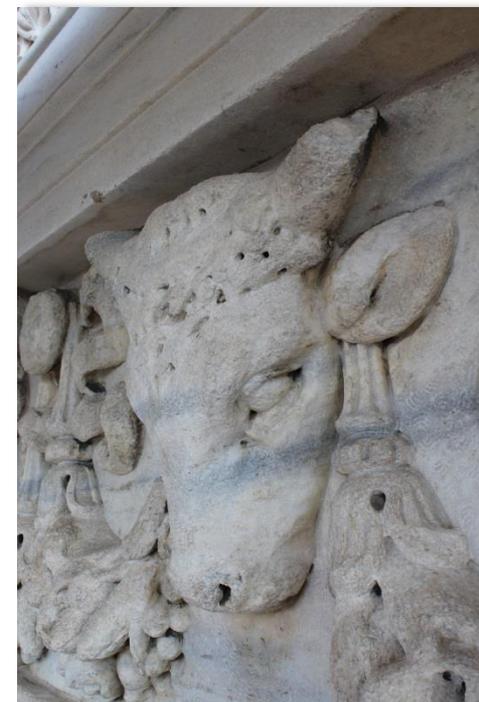

There are ornamental details on the south façade that are not seen on any other part of the Capitol building. These include statues, symbols and animal carvings.

Questions or Comments?

Capitol Complex Tenant Inquiries

Cathy Klima, Communications Officer, Capitol Restoration
Department of Administration
cathy.klima@state.mn.us | 651-201-2627

Press Inquiries

Curt Yoakum, Director, Communications and Legislation
Department of Administration
curtis.yoakum@state.mn.us | 651-201-2771

Visiting the Capitol? See the [Minnesota State Capitol Restoration Project website](#).

To browse planning and communications documents about this project visit the [Minnesota State Capitol Preservation Commission website](#).

Getting Around The Capitol

Nov 24 - 28, 2014



Minnesota State Capitol Restoration Project

Architectural Integrity. Building
Functionality. Life Safety.

What to Expect

The Capitol is an active construction site and your safety is our number one priority. Please stay within the designated public areas.

Interior

- Restrooms are very limited.
- Expect to see temporary walls where construction is present.
- Expect construction workers and machinery, noise and vibration.
- The basement tunnel is open to employees only Aug. 29 – early Dec. Temporary corridors will slightly reconfigure day-to-day to accommodate work areas. Signage will guide you through the corridors.
- An audio recording helps blind and low-vision employees navigate the Capitol tunnel as they enter the Capitol basement from the State Office Building.

Exterior

- Expect scaffolding, chain link fences, machinery, noise, workers and closed sidewalks.

What's Open

- Entrances: South Main Entrance and the accessible Ground Floor Entrance under the South Main Entrance stairs.
- West Wing: 2nd, 3rd floors. Entire North Wing.
- Basement tunnel: Open to employees only effective Aug. 29 – early Dec.
- West elevator, adjacent to South Main Entrance, services Ground through 3rd floors only effective Aug. 29 – mid-Nov.
- Public Restrooms: Unisex restrooms available on 2nd and 3rd floors, both located on the east side of the House Chamber. Employees can also use restrooms next to the Rathskeller.

What's Closed

- Entrances: East Wing, West Wing, University Ave (north side of building).
- Rotunda
- East Wing: All floors.
- West Wing: Ground, 1st Floors.
- Quadriga
- NE circular stairs: Closed to the public, except for emergencies.
- East elevator: All floors.
- Basement tunnel: Closed to the public, effective Aug. 29 – early Dec.
- West elevator: Basement floor only.

Learn the latest about parking, accessibility, news, and FAQs. Visit the [Minnesota State Capitol Restoration Project website](#).
